

Habibur Rahman

From: Md. Sajedul Karim <sajedul@cross-world.com>
Sent: Thursday, October 14, 2021 12:46 PM
To: habib@cross-world.com
Cc: ariful@cross-world.com; zia@cross-world.com; taz@cross-world.com; sultan@cross-world.com; 'Laila Siddika'
Subject: FW: Dhaka-3 DG(350KVA) sync. alignment
Attachments: BOQ For Synchronized work at DKH-03 (1).xlsx; Costing For Synchronized work at DKH-03.xlsx

Dear Sir

Confirmation of new order received. Client will issue PO later.

We need to raise requisition immediately. Need your kind cooperation in this regard.

Best Regards

A. N. M. Sajedul Karim | **CROSS WORLD POWER LTD** | Engineer- Design, Installation & Commissioning | Plot 1/B, Road 90, Gulshan 2, Dhaka 1212, Bangladesh | p: +880 2 5881 6528, 989 1442 | f: +880 2 5881 5160 | Mobile No: +088 01755514809 | e-mail: sajedul@cross-world.com | web: www.cross-world.com

 please consider the environment before printing this email.

From: Md. Sajedul Karim [mailto:sajedul@cross-world.com]
Sent: Wednesday, October 13, 2021 12:38 PM
To: ariful@cross-world.com
Subject: FW: Dhaka-3 DG(350KVA) sync. alignment

Best Regards

A. N. M. Sajedul Karim | **CROSS WORLD POWER LTD** | Engineer- Design, Installation & Commissioning | Plot 1/B, Road 90, Gulshan 2, Dhaka 1212, Bangladesh | p: +880 2 5881 6528, 989 1442 | f: +880 2 5881 5160 | Mobile No: +088 01755514809 | e-mail: sajedul@cross-world.com | web: www.cross-world.com

 please consider the environment before printing this email.

From: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd) [mailto:nakib.muhammad@robi.com.bd]
Sent: Wednesday, October 13, 2021 12:15 AM
To: Md. Sajedul Karim
Cc: Nafiul/Tech/Nafiul Islam (Email: nafiul.islam@robi.com.bd); taz@cross-world.com; zia@cross-world.com; sultan@cross-world.com; 'Md. Osman Ghani'
Subject: RE: Dhaka-3 DG(350KVA) sync. alignment

Dear Sajed vai,

Please process for sync panel , we are processing PO as per BoQ.

Regards,

Nakib Muhammad Abdul Munayem

Planning | Technology


Robi Axiata Limited

Mobile: +8801833181345

57 & 57/A Gulshan South Avenue

Gulshan-1 | Dhaka 1212

www.robi.com.bd



From: Md. Sajedul Karim <sajedul@cross-world.com>

Sent: Monday, October 11, 2021 5:22 PM

To: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd)
<nakib.muhammad@robi.com.bd>

Cc: Nafiul/Tech/Nafiul Islam (Email: nafiul.islam@robi.com.bd) <NAFIUL.ISLAM@robi.com.bd>; taz@cross-world.com; zia@cross-world.com; sultan@cross-world.com; 'Md. Osman Ghani' <osman@cross-world.com>

Subject: RE: Dhaka-3 DG(350KVA) sync. alignment

[THIS IS AN EXTERNAL EMAIL -- BE CAUTIOUS TO OPEN -- VERIFY THE SENDERS E-MAIL ADDRESS]

CAUTION: Do not click links or open attachments unless you recognize the sender and know the content is safe.

Dear Nakib Vai

Please find the BOQ for generator synchronization work as attached. Please feel free to communicate with us with any query

Best Regards

A. N. M. Sajedul Karim | **CROSS WORLD POWER LTD** | Engineer- Design, Installation & Commissioning | Plot 1/B, Road 90, Gulshan 2, Dhaka 1212, Bangladesh | p: +880 2 5881 6528, 989 1442 | f: +880 2 5881 5160 | Mobile No: +088 01755514809 | e-mail: sajedul@cross-world.com | web: www.cross-world.com

 please consider the environment before printing this email.

From: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd)
[<mailto:nakib.muhammad@robi.com.bd>]

Sent: Thursday, October 07, 2021 4:57 PM

To: Md. Hojaifar Rahman; Taz Uddin ; Anindya/Tech/Anindya Kumar Kundu (Email: anindya.kundu@robi.com.bd);
Md. Mijanur Rahman; Syed Mohammad Ali; 'Md. Sajedul Karim'; Taz Uddin ; 'Md. Sajedul Karim'; Ajoy/Tech/Ajoy
Kumar Bhowmick (Email: ajoy.bhowmick@robi.com.bd)

Cc: Nafiul/Tech/Nafiul Islam (Email: nafiul.islam@robi.com.bd); Rezwanul/Tech/AHM Rezwanul Islam (Email: rezwanul.islam@robi.com.bd)

Subject: RE: Dhaka-3 DG(350KVA) sync. alignment


Thanks for joining the meeting.
Please have our decision point:

1. DG sync panel will be ready for 04 DG (including existing 02 DG) and initially 1x350 KVA will be synced with 2x1000 KVA DG (existing).
2. High level operational modality: Initially 1x1000 KVA and 1x350 KVA DG will run as per priority setting, if required any specific DG can be run manually under sync. Modality may change later as per discussion and alignment.
3. In future, we will arrange additional one DG from existing site for more backup purpose.

Dear Mijan vai, Ali vai, Ajoy Da,

As per discussion, please share your go ahead so that Cross World team can arrange material and start control DB manufacturing.

Later CW team will visit for specific location finalization and actual cable measurement purpose.

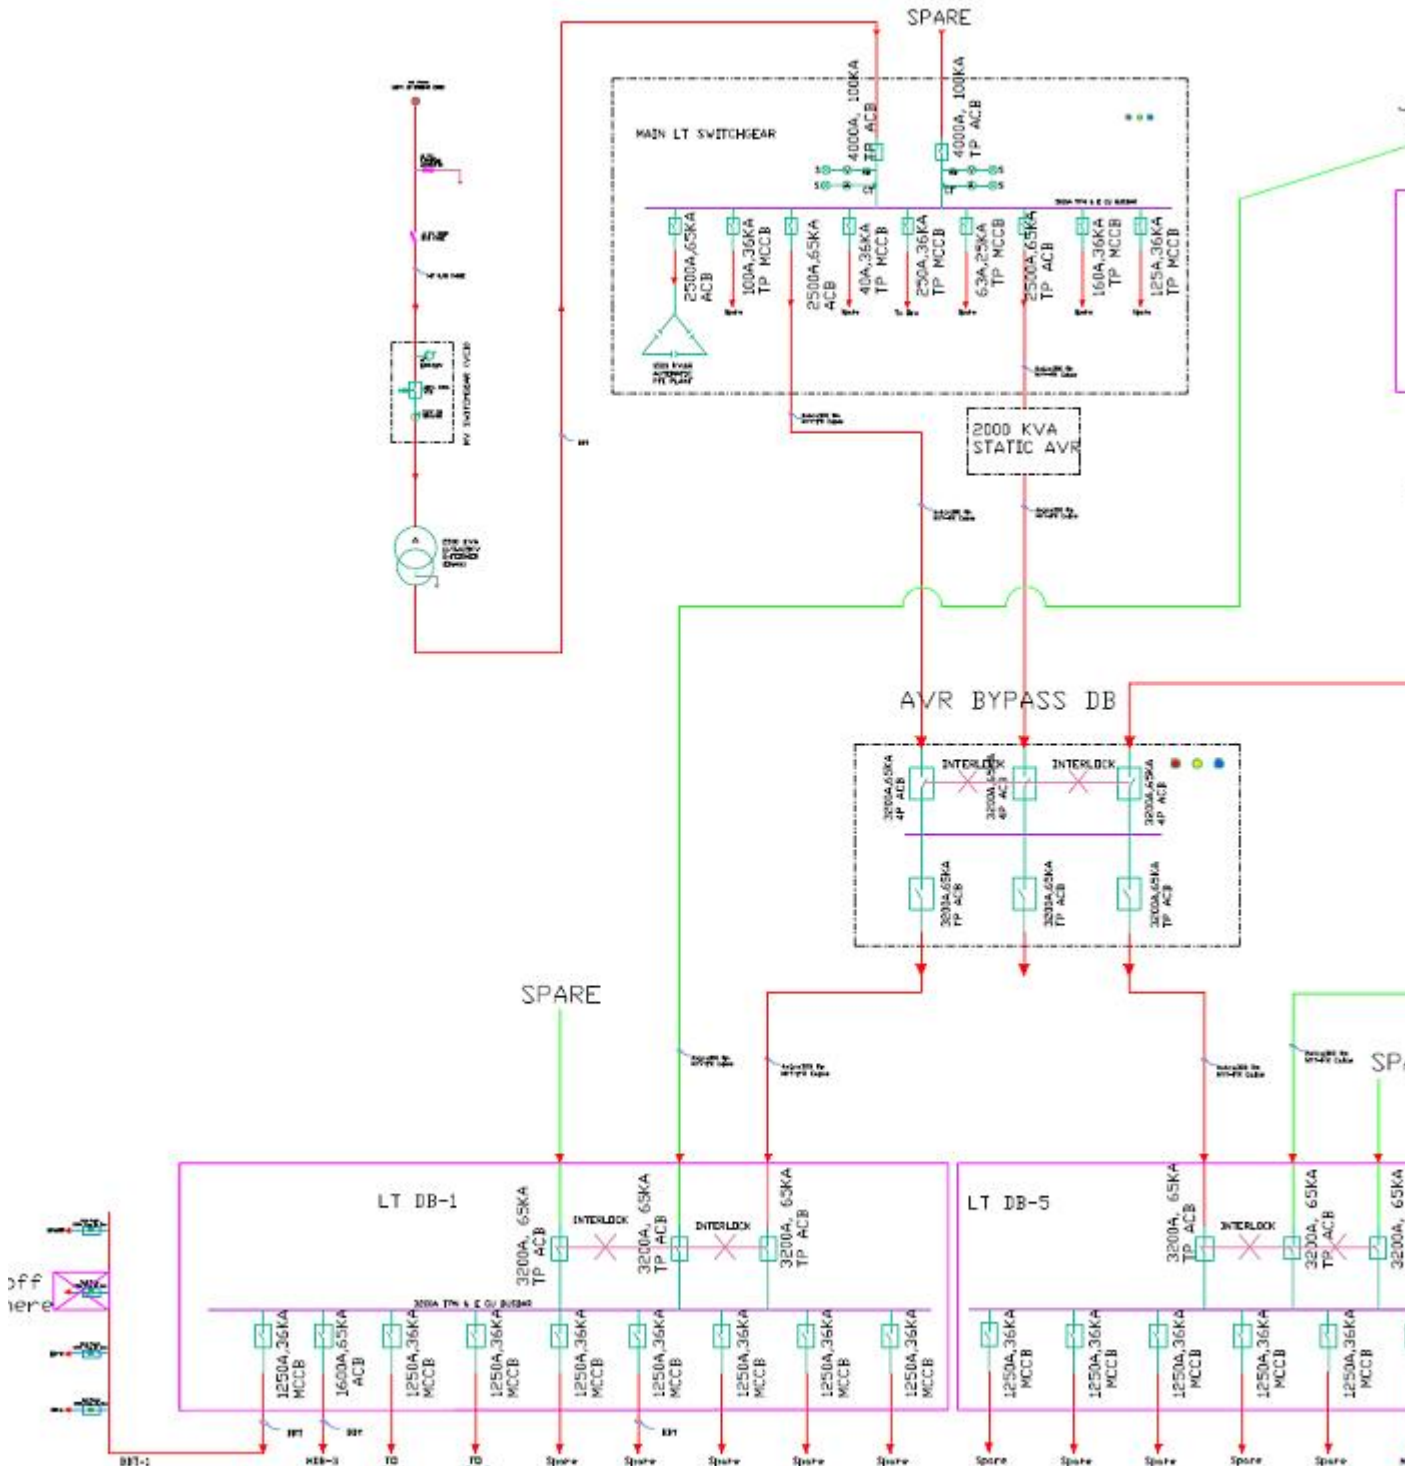

Regards,

Nakib Muhammad Abdul Munayem

Planning | Technology


Robi Axiata Limited

Mobile: +8801833181345

57 & 57/A Gulshan South Avenue

Gulshan-1 | Dhaka 1212

www.robi.com.bd



-----Original Appointment-----

From: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd)

Sent: Wednesday, October 6, 2021 11:30 AM

To: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd); Md. Hojaifar Rahman; Taz Uddin ; Anindya/Tech/Anindya Kumar Kundu (Email: anindya.kundu@robi.com.bd); Md. Mijanur Rahman; Syed Mohammad Ali; 'Md. Sajedul Karim'; Taz Uddin ; 'Md. Sajedul Karim'

Cc: Nafiul/Tech/Nafiul Islam (Email: nafiul.islam@robi.com.bd); Ajoy/Tech/Ajoy Kumar Bhowmick (Email: ajoy.bhowmick@robi.com.bd)

Subject: Dhaka-3 DG(350KVA) sync. Aircon deployment at different sites

When: Thursday, October 7, 2021 12:00 PM-1:00 PM (UTC+06:00) Dhaka.

Where: Microsoft Teams Meeting

Pls join for a short discussion. .

Microsoft Teams meeting

Join on your computer or mobile app

[Click here to join the meeting](#)

Join with a video conferencing device

robivc@m.webex.com

Video Conference ID: 132 618 931 2

[Alternate VTC instructions](#)

[Learn More](#) | [Meeting options](#)

From: Md. Hojaifar Rahman <hojaifar@edotcogroup.com>

Sent: Tuesday, October 5, 2021 8:11 PM

To: Taz Uddin <taz@cross-world.com>

Cc: Nakib/Tech/Nakib Muhammad Abdul Munayem (Email: nakib.muhammad@robi.com.bd)

SI No	Item	Quantity	Unit	Unit Price	Total Price	Remarks
1	Synchronization work (As per attached BOQ)	2	Job	274,615	549,230.90	
2	350 KVA Generator Servicing (As per attached BOQ)	1	job	162,246	162,246	
Total					711,477	

Notes:

1. Servicing cost of 350KVA prior to running is included. If found any problem after servicing during running of the generator, that will be out of this offer scope. CWPL will notify accordingly.
2. Servicing and any installation cost of provisional generator is not included in this offer.
3. Power cable, laying/dismantle charge, cable installation accessories are not included in this offer. CWPL will provide after finalizing generator location & cable route.

CROSS WORLD LIMITED							
BOQ OF Generator Sync Re-installation work at DKH-03							
SL No	DG Spares: Repair/Service Items	Unique SL No(SOR)	UOM	Qty	Unit Price	Total Price	Remarks
1	Generator Synchronized System Display Controller		No	1	156,750	156,750	Not found in SOR
2	Relay12 pin, AC/DC with base	467	No	6	1,733	10,398	Found in SOR
3	Circuit Breaker: 16A, 10 KA DP MCB	198	No	11	774	8,515	Found in SOR
4	Panel Control Cable	232	Meter	100	19	1,900	Found in SOR
5	MGB Bar with required nuts,(replacement of Still channel with Nut & bolt)	459	No	1	1,573	1,573	Found in SOR
6	Cable tie, 12", Black	325	BOX	3	211	633	Found in SOR
7	Tape: Red (Tesa/Nito)	384	Pcs	4	28	112	Found in SOR
8	Sprial		Packet	1	200	200	Not found in SOR
9	Cable tie, 6", White(replacement of Stamp Tie)	334	Pcs	20	100	2,000	Found in SOR
10	Control clip(O-large)		No	12	7	84	Not found in SOR
11	Control clip(O-Small)		No	30	7	210	Not found in SOR
12	Control clip(I)		No	160	7	1,120	Not found in SOR
13	Control clip(U)		No	100	7	700	Not found in SOR
14	PVC Flexible Control Cable, 40/76-1.3 RM		Meter	200	54	10,800	Not found in SOR
15	shild cable		Meter	95	250	23,750	Not found in SOR
16	Current Transformer, 501-1000/5 A	18	No	3	1,400	4,200	Found in SOR
17	Supply and fixing of Power Connection Connector		No	35	62	2,170	Not found in SOR
18	Generator Sync Re-installation work		Job(Per day)	1	20,000	20,000	Not found in SOR
19	GI Box (Made with 18 SWG)(Replacement of controller BOX modification)	2	CFT	25	1,180	29,500	Found in SOR
20	Supply of FR power cable 1*185 rm NYY		Meter		2815	-	Will be given after finalizing of DG location and power cable rating
21	Cable lugs, 185 RM	375	pcs		311	-	Will be given after finalizing of DG location and power cable rating
22	Cable Laying/ Dismantling (185-400 rm), single/ four core	640	Meter		173	-	Will be given after finalizing of DG location and power cable rating
Total Amount (Incl. AIT but Excl. VAT)						274,615.45	

CROSS WORLD LIMITED							
BOQ OF 350 KVA Generator load test work at DKH-03							
SL No	DG Spares: Repair/Service Items	Unique SL No(SOR)	UOM	Qty	Unit Price	Total Price	Remarks
1	Starting Battery, 12 V, 200 Ah, 29 Plate (Brand: Rahimafrooz/Navana/Volvo)		No	2	24700	49,400	Not found in SOR
2	Lube Oil Filter		No	1	3610	3,610	Not found in SOR
3	Fuel Filter		No	2	3458	6,916	Not found in SOR
4	Air Filter		No	1	12825	12,825	Not found in SOR
5	Water Separator Fuel Filter		No	1	2552	2,552	Not found in SOR
6	Lube Oil, (Grade: SAE 15-W-40, Brand: Mobil Delvac)		BOX	65	420	27,300	Not found in SOR
7	Complete Radiator repairing at workshop with Chemical, Water pressor, detergent powder etc including Carrying		Pcs	1	17908	17,908	Not found in SOR
8	Coolant (NALCO-2000)/Quakercity/Golden Gosia		ML	5000	0.71	3,550	Not found in SOR
9	Distilled Water for radiator		Pcs	60	38	2,280	Not found in SOR
10	Emergency Maintenance Charge		Job	3	2660	7,980	Not found in SOR
11	Transportation Charge		Job	3	2375	7,125	Not found in SOR
12	Service Charge for Loading & Unloading in Dhaka Division	698	Job	2	10,400	20,800	Found in SOR
Total Amount (Incl. AIT but Excl. VAT)						162,246	
